FACILITIES LEASE

For all or a portion of the following Site:

Project: Cesar Chavez/Edward Kemble New Construction and Modernization Project
Recorded Addresses: 7495 29th Street Sacramento, CA 95822 and 7500 32nd Street Sacramento, CA 95822
APN: 04901760020000 and 049 01830020000

By and between

Sacramento City Unified School District
5735 47th Avenue
Sacramento, CA 95824

And

[Developer]
[Address]

Dated as of _____, 20__

FACILITIES LEASE

This facilities lease ("Facilities Lease"), dated as of _____, 20__ ("Effective Date"), is made and entered into by and between [Name of Developer] ("Developer"), a [California corporation] duly organized and existing under the laws of the State of [California], as sublessor, and Sacramento City Unified School District, a school district duly organized and validly existing under the laws of the State of California, as sublessee ("District") (together, the "Parties").

RECITALS

WHEREAS, the District is authorized under Section 17406 of the Education Code of the State of California to lease a site to a developer and to have that developer develop and construct the project on the site and to lease back to the District the completed project and site; and

WHEREAS, on the date hereof, the District has leased to Developer two (2) parcels of land. One is located at 7495 29th Street Sacramento, CA 95822, and is known as Edward Kemble Elementary School, and the other is located at 7500 32nd Street Sacramento, CA 95822, and is known as Cesar E Chavez Elementary School. These parcels are particularly described in Exhibit A and shown on Exhibit B attached hereto and incorporated herein by reference ("Site"); and

WHEREAS, District and Developer have executed a site lease at the same time as this Facilities Lease whereby the District is leasing the Site to Developer ("Site Lease"); and

WHEREAS, the District desires to provide for the development and construction of

WHEREAS , the se lection of Developer was conducted in a fair and impartial manner; and

WHEREAS , Developer has reviewed the Lease Documents; and

WHEREAS, Developer represents that it has the expertise and experience to perform the services set forth in this Facilities Lea se; and

WHEREAS , the Parties have performed all acts, conditions and things required by law to exist, to have happened and to have been performed precedent to and in connection with the execution and entering into of this Facilities Lease and all those conditions precedent do exist, h ave happened and have been performed in regular and due time, form and manner as required by law, and the Parties edoaenlsr 0 Tw 3.434 0 4.277:c 0 Tw 3.434 0 17.663

1.6.3 This Facilities Lease.

1.6.4 Easements , rights of way, mineral rights, drilling rights and other rights, reserva tions, covenants, conditions or restrictions which exist of record as of the date of this Facilities Lease .

1.6.5 Easements , rights of way, mineral rights, drilling rights and other rights, reservations, covenants, conditions or restrictions established followin g the date of recordation of this Facilities Lease and to which Developer and the District consent in writing which will not impair or impede the operation of the Site .

003 Tc -0.003 Tw -31.65ite

2. Exhibits

The following Exhibits are attached to and by reference incorporated and made a part of this Facilities Lease:

2.1 Exhibit A -

continue to have and hold a leasehold estate in the Site pursuant to the Site Lease throughout the Term thereof and the Term of this Facilities Lease.

3.3 As to the Site, this Facilities Lease shall be deemed and constitute a sublease.

4. Term

4.1 Facilities Lease is Legally Binding

This Facilities Lease is legally binding on the Parties upon execution by the Parties and the District Board's approval of this Facilities Lease. The "Term" of this Facilities Lease for the purposes of District's obligation to make Lease Payments shall commence on the date when Developer delivers possession of the Project to District and when all improvements to be provided by Developer are determined by the District to be completed as set forth in Exhibit D to this Facilities Lease.

Unless earlier terminated pursuant to the provisions of the Contract Documents, the Term of this Facilities Lease for the purposes of District's obligations to make Lease Payments shall terminate one (1) year thereafter or upon payment of the final lease payment.

4.2 After Developer has

agreement or instrument to which Developer

confirm that those comments are properly incorporated into the final design documents.

10.1.2.3

10.1.3.2.10 Rough-in;

10.1.3.2.11 Finishes;

10.1.3.2.12 Testing;

10.1.3.2.13 Owner and Maintenance Manuals (not less than 2%); and

10.1.3.2.14 Punchlist and District acceptance (not less than 3%).

10.1.4 Construction Schedule and Phasing Plan

Developer shall prepare a preconstruction schedule to guide the design team through to bid dates. That schedule shall show the multiple phases and interrelations of design, constructability review, and estimating. Developer shall also prepare a full construction schedule for the Project detailing the construction activities. Developer shall further investigate, recommend and prepare a schedule for the purchase of materials and equipment requiring long lead time procurement, and coordinate the schedule with the early preparation of portions of the Contract Documents by the Architect.

10.1.5 Construction Planning and Bidding

10.1.5.1 For all of Developer's activities relating to construction planning and bidding, Developer shall comply with all applicable legal requirements, including but not limited to those set forth in Education Code section 17406.

10.1.5.2 Consult with District staff in relation to the existing site. Selected developer should make site visits, as needed to review the current site conditions. During this evaluation, Respondent may make recommendations relating to soils investigations and utility locations and capacities, in order to minimize unforeseen conditions.

10.1.5.3 Attend meetings at the Site with the Architect and the design team as needed.

10.1.5.4 Provide plan review and constructability services with an emphasis on ensuring that the Project can be completed within the established schedule and within the available budget.

10.1.5.5 Provide a detailed analysis of all major Project systems with an emphasis on possible value engineering possibilities.

10.1.5.6 Prepare and distribute specifications and drawings provided by District to facilitate bidding to Developer's subcontractors.

10.1.5.7 Review the drawings and specifications to eliminate areas of conflict and overlapping in the work to be performed by various

subcontractors, and with a view to eliminating change order requests by the Architect or subcontractors.

10.1.5.8 Conduct pre-bid conferences with invitations to Architect and CM firm. Coordinate with District and the Architect in responding to subcontractor questions or providing clarification to all subcontractors.

10.1.5.9 DSA approved plans shall be utilized to receive subcontractor bids and develop the GMP in accordance with the lease-leaseback agreement forms, including the requirement that Developer engage in competitive bidding for subcontractors for all scopes of work on the Project that constitute more than one half of one percent (0.5%) of the GMP. The District representative shall be present during the receipt of bids from subcontractors.

10.1.5.10 Each phase GMP shall be presented to the District in the following manner within a three ring binder as well as submitted electronically as a bookmarked PDF on an external USB drive:

10.1.5.10.1 Cover sheet, signed by Developer indicating the GMP dollar amount with a certification, indicating that the GMP is all inclusive per the plans, specifications and addenda (contract documents). Also include certification stating, "Developer hereby certifies that they have reviewed all subcontractor proposals and whether the subcontractor excluded portions of their scope Developer has included all costs for a complete GMP in accordance with plans, specifications and addenda."

10.1.5.10.2 A bid tabulation sheet indicating the breakdown by subcontractor/trade along with the appropriate general condition amount, other fees (as submitted with the response to the RFQ/P).

10.1.5.10.3 Behind the bid tabulation sheet mentioned in subdivision 10.1.5.5.2 above should be a sheet that indicates what is included in the general conditions, which should match what was submitted in the response to the RFQ/P.

10.1.5.10.4 Copies of all subcontractor bids received divided by trade that corresponds to the final spread sheet with a cover sheet indicating the scope and subcontractors that provided bids as well as those that were asked to bid, but did not submit a proposal. This sheet should have the dollar amounts for each subcontractor that provided a bid with the first column being the proposed subcontractor for that trade.

10.1.5.10.5 Behind subdivision 10.1.5.5.4 above should be the bids for that trade with the proposed subcontractor bid on top and the other subcontractor bids in descending order based on best value score.

10.1.5.10.6 The minimum number of bona fide bids from

provisions as set forth in Exhibit D and/or the Supplementary Conditions (if any), and that complies with all requirements for Commercial General Liability and Automobile Liability and Employers' Liability Insurance.

15.1.2.3 The District, in its sole discretion, may accept the Excess Liability Insurance Policy that brings Developer's primary limits to the minimum requirements herein.

15.1.3 Subcontractor

Developer shall require its Subcontractor(s), if any, to procure and maintain Commercial General Liability Insurance, Automobile Liability Insurance, and Excess Liability Insurance (if Subcontractor elects to satisfy, in part, the insurance required herein by procuring and maintaining an Excess Liability Insurance Policy) with minimum limits at least equal to the amount required of Developer except where smaller minimum limits are permitted as set forth below.

15.1.4 Worke[illegible]

indicating the required coverages have been obtained, and the District has approved these documents.

15.1.7.2 Endorsements, certificates, and insurance policies shall include the following:

15.1.7.2.1 A clause stating

shall have the right to procure the required insurance through a joint powers agency or to self-insure against such losses or portion thereof as is deemed prudent by District.

16. Indemnification and Defense

16.1 To the fullest extent permitted by California law, Developer shall indemnify, keep and hold harmless the District, the Architect(s) and Construction Manager(s), their respective consultants, separate contractors, board members, officers, representatives, agents, and employees, in both individual and official capacities ("Indemnitees"), against all suits, claims, injury, damages, losses, and expenses ("Claims"), including but not limited to attorney's fees and costs, caused by, arising out of, resulting from, or incidental to, in whole or in part, the performance of the Work under this Contract by Developer or its Subcontractors, vendors and/or suppliers. However, Developer's indemnification and hold harmless obligation shall be reduced by the proportion of the Indemnitees' and/or Architect's liability to the extent the Claim(s) is/are caused wholly by the

16.3 Without limitation of the provisions herein, if Developer 's obligation to indemnify and hold harmless the Indemnitees or its obligation

17.2 Total Taking Prior to Project Delivery

If all of the Project and the Site is taken permanently under the power of eminent domain and Developer is still performing the work of the Project and has not yet delivered possession of the Project to District, the Term shall cease as of the day possession shall be so taken. The financial interest of Developer shall be the amount Developer has expended to d ate for work performed on the Project , subject to documentation reasonably satisfactory to the District.

17.3 Partial Taking

If, following delivery of possession of the Project by Developer to District , less than all of the Project and the Site is taken permanently, or if all of the Project and the Site or any part thereof is taken temporarily, un der the power of eminent domain.

17.3.1 ThisJ 0 Tc 0 Tw 1.9642 6 (P)-160.265 0 TdM28.2lF (i)36.4 (k)-3.1 (t)-8.i (l)]TJ 0(i)-11.2 8nnttms

19.3.1 Repair the Project to full use .

19.3.2 Replace the Project, at the District's sole cost and expense, with property of equal or greater value to the Project immediately prior to the time of the destruction or damage, and that replacement, once completed, shall be substituted in this Facilities Lease by appropriate endorsement; or

19.3.3 Exercise the District's purchase optio *to **Exhibit D** to the Facilities Lease* n as indicated in the GMP provisions indicated in Exh ibit C to this Facilities Lease.

19.4 The District shall notify Developer of which course of action it desires to take within thirty (30) days after the occurrence of the destruction or damage . The Net Proceeds of all insurance payable with respect to the Project shall be available to the District and shall be used to discharge the District's obligations under this Section.

20. Access

20.1 By Developer

Developer shall have the right at all reasonable times to enter upon the Site to construct the Project pursuant to this Facilities Lease. Following the acceptance of the Project by District, Developer may enter the Project at reasonable times with advance notice and arrangement with District for purposes of making any repairs required to be made by Developer .

20.2 By Di strict

The District shall have the right to enter upon the Site at all times. District shall comt101 Tw 0.265nPrr

in connection with any assignment by Developer to a lender for purposes of financing the Project as long as there are not additional costs to the District.

22. Termination, Default And Suspension

22.1 Termination; Lease Terminable Only As Set Forth L7249 ((s)-5.11.7 (rm)-Gv o)-1.8 (38.4830 Tc 0 Tw 27.95

written assurances from Developer of performance of Work and a written plan from Developer to remedy any potential default under the terms of this Co ntract that the District may advise Developer of in writing. Developer shall, within ten (10) calendar days 0.6 (f)-2.6.8 (o1(p)-20.o8w1ti)-20.1 2229.6 ( )]TJ 0.0.1 2229.6 ( )iser to(.)

22.3.1.10 Developer or its Subcontractor(s) is/are otherwise in breach, default , or in substantial violation of any provision of this Facilities Lease, including but not limited to a lapse in licensin.8 (n)-179t le

22.3.3.6 In the eve nt that the Site Lease and Facilities Lease are terminated for any reason, no allowances or compensation will be granted for the loss of any anticipated profit by Developer or any impact or impairment of Developer's bonding capacity.

22.3.3.7 If the expense to the District to finish the Work exceeds the unpaid Guaranteed Maximum Price, Developer and Surety shall pay difference to District within twenty -one (21) days of District's requee1.6 2a2

22.4.3 Within 30 days of the notice, D eveloper shall submit to the District a payment application for the actual cost for labor, materials, and services performed, including all Developer's and Subcontractor(s)' mobilization and/or demobilization costs, that is unpaid. Developer shall have no claims against the District except for the actual cost for labor, materials, and services performed that adequately documented through timesheets, invoices, receipts, or otherwise. District shall pay all undisputed invoice(s) for work performed until the notice of termination .

22.4.4 Under a termination for convenience, the District retains the right to all the options available to the District if there is a termination for cause .

22.5 Developer Remedies Upon District Default

22.5.1 Events of Default by District Defined

The following shall be "Events of Default" of the District under this Facilities Lease. The terms "Event of Default" and "Default," whenever they are used as

22.5.2.1.2 If an appraiser cannot be agreed to, an amount equal to the mean between a District appraisal and a Developer appraisal for the Project and Site, both prepared by MAI-certified appraisers.

22.5.2.2 District's obligation to make the payments required pursuant to the GMP provisions indicated in Exhibit C sh sitxit 9 (x)21 Tf 0 Tc 4.976 0

22.6.1.1 Section 4410 of the Government Code states:

In the event a national emergency occurs, and public work, being performed by contract, is stopped, directly or indirectly, because of the freezing or diversion of materials, equipment or labor, as the result of an order or a procla mation of the President of the United States, or of an order of any federal authority, and the circumstances or conditions are such that it is impracticable within a reasonable time to proceed with a substantial portion of the work, then the public agency and the contractor may, by written agreement, terminate said contract.

22.6.1.2 Section 4411 of the Government Code states:

Such an agreement shall include the terms and conditions of the termination of the contract and provision for the payment of compensation or money, if any, which either party shall pay to the other or any other person, under the facts and circumstances in the case.

22.6.2 Compensation to Developer shall be determined at the sole discretion of District on the basis of the reasonable value of the Work done, including preparatory work. As an exception to the foregoing and at the District's discretion, in the case of any fully completed separate item or portion of the Work for which there is a separate previously submitted unit price or item on the accep ted schedule of values, that price may control. The District, at its sole discretion, may adopt the Schedule of Values Price as the value of the work done or any portion thereof.

22.7 Suspension of Work

22.7.1 District in its sole discretion may suspend, delay or interrupt the Work in whole or in part for such period of time as the District may determine upon three (3) days written notice to Developer.

22.7.1.1 An adjustment may be made for changes in the cost of performance of the Work caused by any suspension, delay or interruption. No adjustment shall be made to the extent:

22.7.1.1.1 That performance is, was or would have been so suspended, delayed or interrupted by another cause for which Developer is responsible; or

22.7.1.1.2 That an equitable adjustment is made or denied under another provision of the Site Lease or the Facilities Lease; or

22.7.1.1.3 That the suspension of Work was the direct or indirect result of Developer’s failure to perform any of its obligations hereunder.

22.7.1.1.4 The delay could n ot have been avoided or mitigated by Developer's reasonable diligence.

27. Severability

In the event any provision of this Facilities Lease shall be held invalid or unenforceable by any court of competent j urisdiction, that holding shall not invalidate or render unenforceable any other provision hereof, unless elimination of the invalid provision materially alters the rights and obligations embodied in this Facilities Lease or the Site Lease .

28. Amendments,

EXHIBIT A

LEGAL DESCRIPTION OF SITE

Attached is the Legal Description for:

Project: Cesar Chavez/Edward Kemble New Construction and Modernization Project
Address es : 7495 29 th Street Sacramento, CA 95822 and 7500 32 nd Street Sacramento, CA 95822
APN: 04901830020000

POR LOT 'A' MEADOWVIEW TERRACE UNIT NO 4 DES AS LYING W OF 32ND ST S OF TORRENCE AVE & N OF A LI NE WHICH BEARS N 86%57'23" E FROM THE NW COR OF LOT
es

APN: 04d 0183002000-12.1 (T)-224 >>BDC 0301 0 Tw 8.952 0 Td ( )Tj EMC 1P <</MCID(L)-0.00 Tf -12.41 -1.217 Td (

EXHIBIT B

DESCRIPTION OF PROJECT

Attached is a map or diagram of the Site that is subject to this Facilities Lease and upon which Developer will construct the Project.

<INSERT>

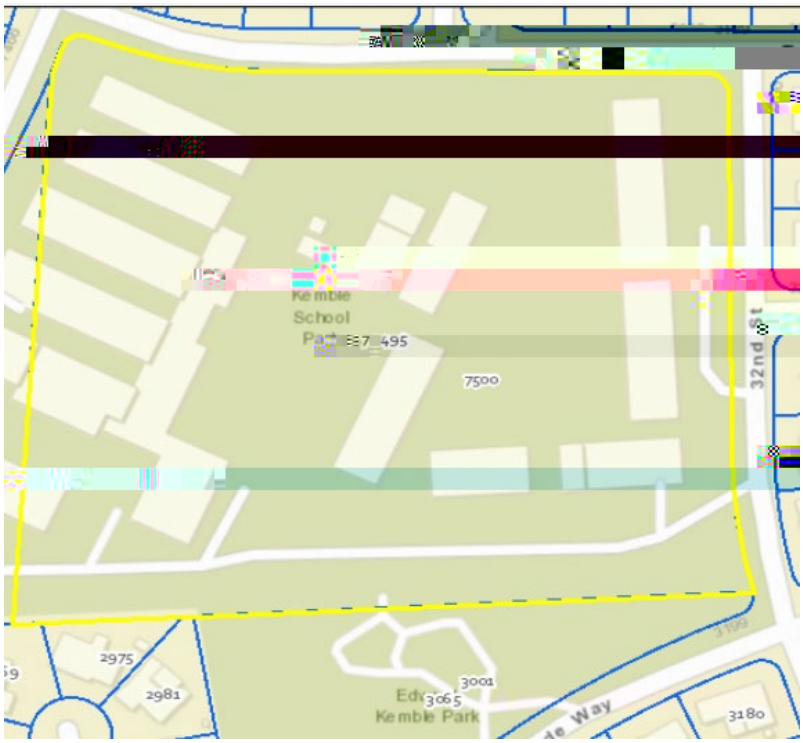

EXHIBIT C

GUARANTEED MAXIMUM PRICE AND
OTHER PROJECT COST, FUNDING, AND PAYMENT PROVISIONS

Attached are the terms and provisions related to Site Lease payments, the Facilities Lease, the Guaranteed Maximum Price and other related cost, funding, and payment provisions.

EXHIBIT D

GENERAL CONSTRUCTION PROVISIONS

Attached are the general construction terms and conditions for the Project.

EXHIBIT G

SCHEDULE OF VALUES

Attached is a detailed Schedule of Values that complies with the requirements of the Construction Provisions (Exhibit "D") and that has been approved by the District.

[To Be Attached Via Addendum .]

EXHIBIT H

PROJECT LABOR AGREEMENT

Attached is the Project Labor Agreement applicable to this Project.
